

Sprint 2 Week 1 — Task Management Implementation Acceptance Review

Project: Intern Management System for Social Enterprise Workforce Development

Client: Food Systems Collective (FSC)

Team: Team 40 / Team B

Role: Business Analyst

Business Analyst: Shakthijhaa Sivagnanam

Student ID: s4065078

Task: [ACCEPTANCE VALIDATION] - Task Management Implementation Acceptance Review : 120

Sprint: Sprint 2 — Week 1

Review date: 20 September 2026

1. Purpose and Review Basis

This document records the BA acceptance review of the completed Sprint 2 Week 1 Task Management vertical slice against the previously approved Week 1 Implementation Clarifications and Acceptance Matrix. The review is based on the available implementation evidence, demonstrated user flows, screenshots, observed system behaviour, test outcomes and implementation handoff information.

Direct Supabase credentials are not required for this BA review. Where persistence is relevant, the acceptance finding is based on implementation evidence showing the created task in the shared tasks table with the expected stored values. This follows the task instruction that the BA does not need direct database configuration access.

2. Evidence Reviewed

- Approved BA source of truth: Sprint 2 Week 1 — Task Management Vertical Slice Implementation Clarifications & Acceptance Matrix.
- Implementation evidence: Sprint 2 Week 1 Task Management functional-test results and screenshots, dated 20 September 2026.
- Demonstrated Mentor-to-Intern Task Management user flow and observed implementation behaviour.
- Relevant Sprint 1 close-out / Sprint 2 handoff information for shared identity, role ownership and status expectations.

Evidence rule: PASS is recorded only where the implementation evidence demonstrates the approved behaviour. FAIL is reserved for demonstrated behaviour that contradicts an approved requirement. BLOCKED is used where the available evidence is insufficient to verify a requirement. Optional enhancements are not recorded as Core MVP defects.

3. Acceptance Review Summary

PASS	FAIL	BLOCKED	Confirmed Core MVP defects
9	0	3	0

Overall acceptance position: The demonstrated Week 1 functional slice is accepted for the behaviours supported by the implementation evidence. The three BLOCKED items are evidence gaps for negative authorization/security scenarios and are not confirmed implementation failures.

4. Acceptance Matrix

AC ID	Acceptance focus	Result	Evidence basis	BA finding
W1-AC01	Mentor creates a valid task	PASS	Implementation evidence shows successful task creation and confirmation.	Meets approved Week 1 requirement.
W1-AC02	Required-field validation	PASS	Incomplete task form is rejected with clear validation feedback.	Meets approved Week 1 requirement.
W1-AC03	Priority validation	PASS	UI provides Low / Medium / High; Medium is stored in the demonstrated test.	Meets approved Week 1 requirement.
W1-AC04	Assigned By is system-derived	PASS	Mentor identity is shown as Assigned By without a second manual Mentor selector.	Meets approved Week 1 requirement.
W1-AC05	Automatic initial Assigned status	PASS	Created task is shown in shared tasks-table evidence and the Intern view with status Assigned.	Meets approved Week 1 requirement.
W1-AC06	Mentor assignment access restriction	BLOCKED	Positive Mentor flow is demonstrated; no negative unauthorized/out-of-relationship assignment result is available.	Not enough evidence to verify; follow-up required, not a confirmed defect.
W1-AC07	Intern views assigned task	PASS	Example_20 Sep appears in the Intern My Tasks list with correct status and priority.	Meets approved Week 1 requirement.
W1-AC08	Unrelated task access denied	BLOCKED	No negative cross-Intern access test is included in the evidence set.	Not enough evidence to verify; follow-up required, not a confirmed defect.
W1-AC09	Intern starts work: Assigned → In Progress	PASS	Start task changes the task from Assigned to In Progress.	Meets approved Week 1 requirement.
W1-AC10	No Intern self-completion in Week 1 slice	PASS	Demonstrated Intern flow exposes Start task only; later submission/completion is outside this slice.	Meets approved Week 1 requirement.
W1-AC11	Shared IMS identity/account continuity	PASS	UI/handoff evidence shows account/profile information comes from the shared IMS and Assigned By resolves from the current account.	Meets approved Week 1 requirement.

W1-AC12	Backend authorization on task requests	BLOCKED	Backend authorization is required, but no negative server-side authorization result is available.	Not enough evidence to verify; follow-up required, not a confirmed defect.
---------	--	---------	---	--

5. Detailed BA Findings

5.1 Mentor Task Assignment and Required Fields — PASS

The implementation evidence shows the Mentor assignment form and a successful task creation. The required Week 1 fields are represented: Task Title, Description, Due Date, Assigned Intern and Priority. Assigned By is presented from the active account rather than as a second Mentor selector. The evidence also shows an incomplete form being rejected with a required-fields message.

W1-AC01 — PASS | W1-AC02 — PASS | W1-AC03 — PASS | W1-AC04 — PASS

5.2 Automatic Initial Status — PASS

The created Example_20 Sep task is evidenced with initial status Assigned. The shared tasks-table evidence records Assigned, and the Intern My Tasks view displays the same task as Assigned before work begins. This matches the frozen Week 1 rule that the initial status is system-established rather than manually selected by the Mentor.

W1-AC05 — PASS

5.3 Intern Task Visibility and Task Detail — PASS

The Intern My Tasks view shows Example_20 Sep with the expected due date, Assigned status and Medium priority. Opening the task shows the stored title, description, due date, Assigned By, priority and status. The demonstrated behaviour matches the approved Intern task-viewing requirements.

W1-AC07 — PASS

5.4 Assigned → In Progress — PASS

The implementation evidence shows the Intern selecting Start task while the task is Assigned. The task then changes to In Progress. This matches the confirmed Week 1 vertical-slice status rule.

W1-AC09 — PASS

5.5 No Intern Self-Completion — PASS

The demonstrated Intern Task Detail exposes the Week 1 start-work action and limits this slice to Assigned → In Progress. No direct Intern completion control is shown. Submission and completion are later workflow stages and are therefore not treated as missing Week 1 functionality.

W1-AC10 — PASS

5.6 Shared IMS Identity Continuity — PASS

The Mentor assignment UI states that account information is loaded from shared IMS account/profile data and resolves the current Mentor as Assigned By. The available implementation and handoff evidence therefore supports shared identity reuse for the demonstrated slice.

W1-AC11 — PASS

5.7 Negative Role / Resource Authorization — BLOCKED

The implementation evidence demonstrates the valid Mentor and Intern paths, but no negative result is available showing an unauthorized user or unrelated Mentor/Intern relationship being rejected. This is recorded as BLOCKED rather than FAIL.

W1-AC06 — BLOCKED | W1-AC08 — BLOCKED

5.8 Backend Authorization — BLOCKED

The approved BA requirement states that role/resource authorization must be enforced by the backend and not only by UI visibility. A negative server-side authorization result is not available in the current evidence set. This remains a verification gap for implementation follow-up.

W1-AC12 — BLOCKED

6. Core MVP Defect Assessment and Follow-up

Confirmed Core MVP defects: 0. No demonstrated Week 1 behaviour contradicts the approved business rules in the implementation evidence. The remaining items are verification gaps, not confirmed requirement defects.

ID	Finding	Priority	Required follow-up
FV-01	Mentor / out-of-relationship negative assignment test not provided.	Medium	Implementation follow-up: provide one negative authorization test or screenshot/log showing the request is denied.
FV-02	Cross-Intern unrelated task access denial not demonstrated.	High	Implementation follow-up: provide a negative resource-ownership test before access control is treated as fully verified.
FV-03	Backend authorization not directly demonstrated.	High	Provide server/API authorization evidence for a restricted task request; direct BA database credentials are not required.

7. Optional / Later Behaviour Not Recorded as Defects

- Task Submission and the Submitted → Completed lifecycle are later workflow stages and are not missing Week 1 Task Management functionality.
- Weekly Progress behaviour is outside this acceptance slice.
- Reverse, skip, reopen and post-completion status transitions are not part of the confirmed Week 1 forward flow.
- Optional UI polish, sorting/filtering, dashboard enhancements or visual refinements are not recorded as Core MVP defects.
- Direct BA Supabase credentials are not required for this acceptance review where sufficient implementation evidence is available.

8. DEV / PM Handoff

- Accepted for the demonstrated Week 1 functional slice: Mentor task creation, required-field validation, Priority, system-derived Assigned By, automatic Assigned status, Intern task visibility/detail and Assigned → In Progress.

- Follow-up evidence required: negative Mentor/resource-access tests and backend authorization evidence. These are verification gaps, not currently demonstrated functional failures.
- No optional or later-sprint enhancement is recorded as a Core MVP defect.

9. Planner Checklist Completion

[x] Review Mentor Task Assignment against the confirmed Week 1 acceptance criteria

Completed through the acceptance matrix and detailed Mentor Task Assignment findings.

[x] Review required fields, Priority, Assigned By and automatic Assigned behaviour

Completed; each item is assessed separately with implementation evidence and a recorded result.

[x] Review Intern task visibility, task details and Assigned → In Progress behaviour

Completed; Intern list, Task Detail and the Start task status transition are evidenced and recorded PASS.

[x] Compare demonstrated implementation behaviour with the confirmed business rules

Completed through the expected-versus-demonstrated acceptance matrix and detailed findings.

[x] Record Pass / Fail / Blocked findings and identify requirement-level defects

Completed: 9 PASS, 0 FAIL and 3 BLOCKED; no confirmed Core MVP requirement defect identified.

[x] Record Pass/Fail with evidence and prioritise true requirement defects

Completed through the evidence references and follow-up table; verification gaps are prioritised without treating optional enhancements as defects.

10. BA Acceptance Outcome

The Week 1 Task Management vertical slice is accepted for the demonstrated functional behaviour. The implementation evidence shows that the approved positive Mentor-to-Intern flow is consistent with the confirmed business rules. No confirmed Core MVP defect was found in the tested scenarios.

Three negative/security acceptance areas remain BLOCKED because the required negative authorization evidence is not yet available. These items should be verified through implementation authorization testing. The acceptance review remains complete because the task explicitly requires clear PASS, FAIL and BLOCKED classification and does not require direct BA database configuration access.

Appendix A — Implementation Evidence

The screenshots below document the implementation states used to support the acceptance findings.

This screenshot shows a web form for assigning a task. The form includes several required fields marked with an asterisk: a task title field, a description field, a due date field (showing 20/09/2026), and an assigned intern dropdown menu (showing 'Select an intern...'). Below these is a priority selection section with buttons for 'Low', 'Medium' (which is selected), and 'High'. The 'Assigned by' field shows 'Test Connection (you)'. A red error message at the bottom states 'Please complete all required fields.' and an 'Assign task' button is located in the bottom right corner.

Figure 1. Valid Mentor Task Assignment input before submission.

A separate incomplete submission was attempted to confirm that required-field validation prevents task creation.

This screenshot shows the form after an attempt at submission. The 'Assigned by' field still shows 'Test Connection (you)'. The 'Assign task' button is present. A green success message at the bottom states '✓ Task assigned to Test Connection (Medium priority).', indicating that the system accepted the submission despite the missing task title and description.

Figure 2. Required-field validation prevents incomplete task creation.

After valid submission, the interface displayed a success confirmation and reset the form for the next assignment.

This screenshot shows the interface after a successful submission. The top navigation bar includes 'IMS' and a 'Mentor' profile icon. Below the navigation bar are two tabs: 'Assign Task' (which is active) and 'Review Progress'. The 'Assign task' section contains the same form as in Figure 1, but it has been reset. The 'Task title' field now contains 'Example_20 Sep', the 'Description' field contains 'Example_20 Sep', and the 'Due date' field shows 21/09/2026. The 'Assigned intern' dropdown now shows 'Test Connection'. The 'Priority' section still has 'Medium' selected. The 'Assign task' button is still present.

Figure 3. Successful Mentor Task Assignment confirmation and form reset.

04255a8d-de04-4d5e-85e1-52d48d11	2026-09-19 12:35:38.676752	Shared Data Test	Testing assignment using Team A acco	2026-09-20 00:00:00+00	In Progress
251fe299-97a1-48fb-8407-d7aa068f4e	2026-09-10 06:01:59.714025	Test Sprint 2 Task	Test task for Team 40 database connec	NULL	In Progress
273b05a4-43d7-4bb2-ac8d-360edefc	2026-09-19 12:03:31.482316	UX Assignment Test	Testing updated Mentor assignment U>	2026-09-20 00:00:00+00	In Progress
6de07b90-c810-4e04-9820-09f670b	2026-09-20 08:42:35.00585	Example_20 Sep	Example_20 Sep	2026-09-21 00:00:00+00	Assigned
846840f8-49fc-43d3-b0b6-3b9cf97a	2026-09-19 16:28:31.801671	Review task	Task created for review	2026-09-22 00:00:00+00	In Progress

Figure 4. Supabase tasks table confirms the new Example_20 Sep task was persisted with status Assigned.

The same database record showed Medium priority together with stored assigned_intern_id and assigned_by_mentor_id references.

The Intern My Tasks view was then opened. Example_20 Sep appeared in the list with the expected due date, Assigned status and Medium priority.

Workspace
My Tasks
Weekly Progress

My Tasks

04255a8d
Shared Data Test
Due 20/9/2026

In Progress

High priority

273b05a4
UX Assignment Test
Due 20/9/2026

In Progress

High priority

6de07b90
Example_20 Sep
Due 21/9/2026

Assigned

Medium priority

846840f8
Review task
Due 22/9/2026

In Progress

High priority

251fe299
Test Sprint 2 Task
Due No due date

In Progress

High priority

Task visibility is scoped to the current Intern.

Figure 6. Intern My Tasks view shows Example_20 Sep with Assigned status and Medium priority.

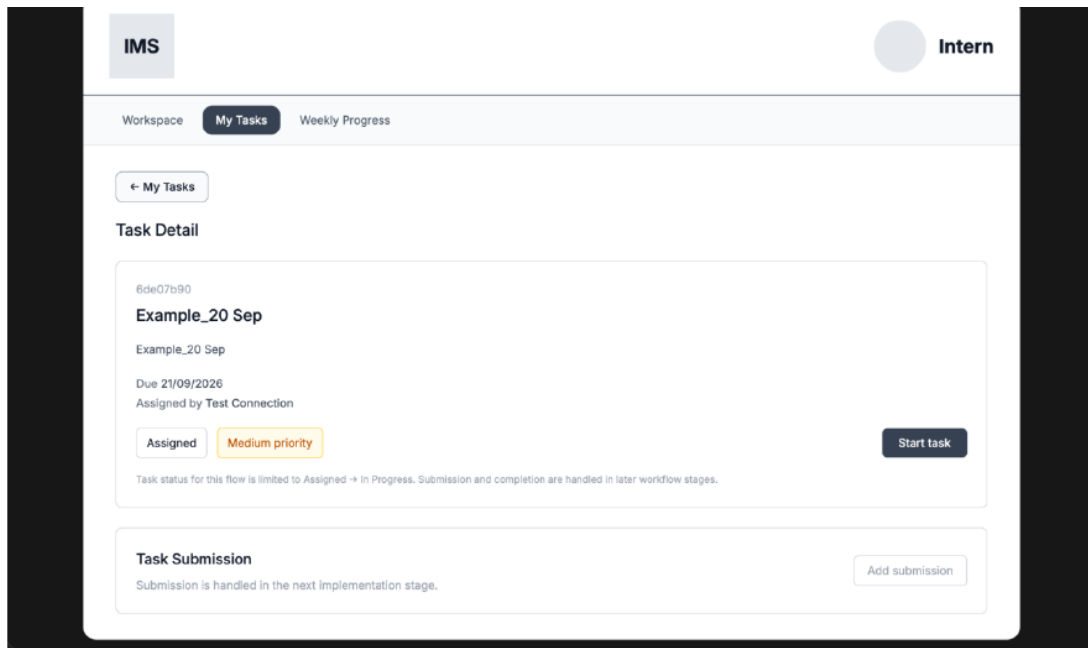


Figure 7. Intern Task Detail shows the stored task data before starting work.

Selecting Start task successfully changed the task status to In Progress.

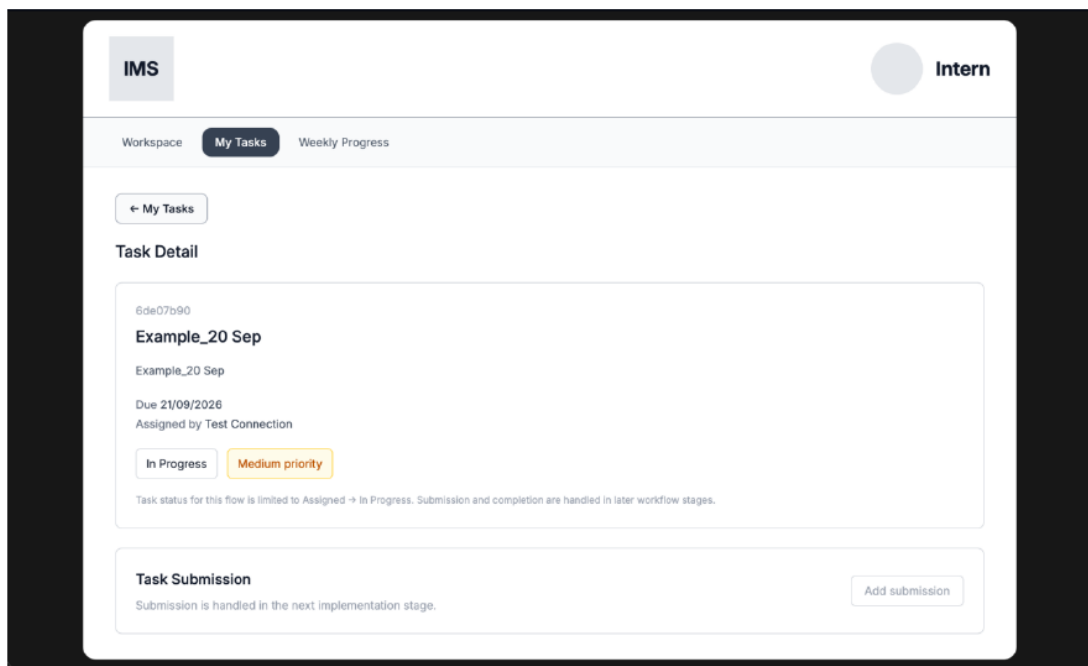


Figure 8. Task status successfully changes from Assigned to In Progress.
